

ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter	
									Mar	Oct
1	1	0%		ADOT Legacy System Replacement	462,826 hrs	Wed 4/2/14	Fri 6/25/21	No		
2	1.1	0%		Project Management Team	79,650 hrs			No		
3	1.1.1	0%		Project Management High Level Estimated Hours	79,650 hrs			No		
4	1.1.2	0%		Project Management	0 hrs			No		
32	1.1.3	0%		Scope Management	0 hrs			No		
60	1.1.4	0%		Change Management	0 hrs			No		
67	1.1.5	0%		Time Management	0 hrs			No		
70	1.1.6	0%		Quality Management	0 hrs			No		
91	1.1.7	0%		Stakeholder Management	0 hrs			No		
112	1.1.8	0%		Issue Management	0 hrs			No		
120	1.1.9	0%		Risk Management	0 hrs			No		
128	1.1.10	0%		Task Management	0 hrs			No		
140	1.1.11	0%		Financial Management	0 hrs			No		
222	1.1.12	0%		Human Resource Management	0 hrs			No		
278	1.1.13	0%		Testing Management	0 hrs			No		
291	1.1.14	0%		Anomaly Management	0 hrs			No		
295	1.1.15	0%		Contract Management	0 hrs			No		
304	1.1.16	0%		Employee Readiness Management (Training)	0 hrs			No		
737	1.1.17	0%		Organizational Change Management (OCM)	0 hrs			No		
812	1.1.18	0%		Data Management	0 hrs			No		
815	1.2	0%		Technical	50,850 hrs			No		
816	1.2.1	0%		Technical High Level Estimated Hours	50,850 hrs			No		
817	1.2.2	0%		Project Infrastructure Preparation	0 hrs			No		
946	1.2.3	0%		Environment Infrastructure Assessment	0 hrs			No		
952	1.2.4	0%		Technical Infrastructure Preparation	0 hrs			No		
1139	1.2.5	0%		Operations Management	0 hrs			No		
1144	1.3	0%		Foundation	41,850 hrs			No		
1145	1.3.1	0%		Foundation High Level Estimated Hours	41,850 hrs			No		
1146	1.3.2	0%		Security Architecture	0 hrs			No		
1155	1.3.3	0%		Cache Architecture	0 hrs			No		

ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter		13
									Mar	Oct	
1159	1.3.4	0%		Logging and Auditing	0 hrs			No			
1162	1.3.5	0%		Messaging Architecture	0 hrs			No			
1163	1.3.6	0%		Information Architecture	0 hrs			No			
1167	1.3.7	0%		Reporting Architecture	0 hrs			No			
1168	1.3.8	0%		Interface Architecture	0 hrs			No			
1169	1.3.9	0%		Printing Architecture	0 hrs			No			
1170	1.3.10	0%		Batch Architecture	0 hrs			No			
1183	1.3.11	0%		Maintenance, Support, and Enhancement	0 hrs			No			
1184	1.4	0%		Cross Functional	33,075 hrs			No			
1185	1.4.1	0%		Cross Functional High Level Estimated Hours	33,075 hrs			No			
1186	1.4.2	0%		Customer	0 hrs			No			
1199	1.4.3	0%		Office Queue Management	0 hrs			No			
1200	1.4.4	0%		Exception Management	0 hrs			No			
1204	1.4.5	0%		Sanctions - Compliance	0 hrs			No			
1212	1.4.6	0%		Case Management	0 hrs			No			
1216	1.4.7	0%		Workflow / Work In Progress	0 hrs			No			
1219	1.4.8	0%		Correspondence	0 hrs			No			
1224	1.4.9	0%		Document Management	0 hrs			No			
1228	1.4.10	0%		Scheduling	0 hrs			No			
1233	1.4.11	0%		Inventory	0 hrs			No			
1241	1.4.12	0%		Configuration Management	0 hrs			No			
1244	1.4.13	0%		Notes / Comments Management	0 hrs			No			
1247	1.4.14	0%		MVR	0 hrs			No			
1250	1.4.15	0%		Imaging	0 hrs			No			
1251	1.4.16	0%		Business Rules Engine	0 hrs			No			
1252	1.4.17	0%		Fee Management	0 hrs			No			
1253	1.4.18	0%		Configuration Management	0 hrs			No			
1254	1.4.19	0%		Enforcement Consolidated Portal (POE)	0 hrs			No			
1255	1.4.20	0%		PC Audit (PC)	0 hrs			No			
1256	1.4.21	0%		Miscellaneous	0 hrs			No			
1257	1.4.21.1	0%		Appeals	0 hrs			No			

ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter		13
									Mar	Oct	
1258	1.4.21.2	0%		Appointments	0 hrs			No			
1259	1.4.21.3	0%		Audit	0 hrs			No			
1260	1.4.21.4	0%		Audit - Licensing Reports	0 hrs			No			
1261	1.4.21.5	0%		Customer Summary	0 hrs			No			
1262	1.4.21.6	0%		Customer Transaction Inquiry	0 hrs			No			
1263	1.4.21.7	0%		Fines	0 hrs			No			
1267	1.4.21.8	0%		Full File Extraction	0 hrs			No			
1268	1.4.21.9	0%		Group Definition	0 hrs			No			
1269	1.4.21.10	0%		Hearings	0 hrs			No			
1270	1.4.21.11	0%		Product Inquiry	0 hrs			No			
1271	1.4.21.12	0%		Productivity by Transaction	0 hrs			No			
1272	1.4.21.13	0%		Productivity by User	0 hrs			No			
1273	1.4.21.14	0%		Productivity by User/Transaction	0 hrs			No			
1274	1.4.21.15	0%		Queue Management	0 hrs			No			
1275	1.4.21.16	0%		Role Definition	0 hrs			No			
1276	1.4.21.17	0%		Transaction History	0 hrs			No			
1277	1.4.21.18	0%		Transaction Summary	0 hrs			No			
1278	1.4.21.19	0%		VOID	0 hrs			No			
1279	1.4.22	0%		Maintenance, Support, and Enhancement	0 hrs			No			
1280	1.5	0%		Cash Drawer / Finance	24,975 hrs			No			
1281	1.5.1	0%		Finance Product High Level Estimated Hours	24,975 hrs			No			
1282	1.5.2	0%		Phase Initiation	0 hrs	Wed 4/2/14	Wed 4/2/14	Yes			
1283	1.5.3	0%		Refunds	0 hrs			No			
1284	1.5.4	0%		VOID	0 hrs			No			
1285	1.5.5	0%		Overrides / Adjustments	0 hrs			No			
1286	1.5.6	0%		Statement	0 hrs			No			
1290	1.5.7	0%		Deposit Slip	0 hrs			No			
1291	1.5.8	0%		Bank Reconciliation	0 hrs			No			
1292	1.5.9	0%		Distribution - TARGATS	0 hrs			No			
1293	1.5.10	0%		Sweep	0 hrs			No			
1294	1.5.11	0%		Adjust Journal Entry	0 hrs			No			

ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter	
									Mar	Oct
1295	1.5.12	0%		NSF	0 hrs			No		
1296	1.5.13	0%		NSF Correspondence	0 hrs			No		
1297	1.5.14	0%		Finance Inquiry	0 hrs			No		
1310	1.5.15	0%		MV Fines	0 hrs			No		
1314	1.5.16	0%		MV Collections	0 hrs			No		
1319	1.5.17	0%		Cash Drawer	0 hrs			No		
1326	1.5.18	0%		Escrow	0 hrs			No		
1331	1.5.19	0%		Fuel Tax	0 hrs			No		
1335	1.5.20	0%		Reports	0 hrs			No		
1339	1.5.21	0%		Cross Functional Integration	0 hrs			No		
1348	1.5.22	0%		User Acceptance Testing	0 hrs	Fri 7/10/15	Fri 7/10/15	Yes		
1349	1.5.23	0%		Employee Readiness	0 hrs	Fri 7/10/15	Fri 7/10/15	Yes		
1354	1.5.24	0%		Deployment	0 hrs			No		
1366	1.5.25	0%		Activation	0 hrs	Fri 1/8/16	Fri 1/8/16	Yes		
1367	1.5.26	0%		Stabilization	0 hrs			No		
1368	1.5.27	0%		Transition	0 hrs	Mon 6/27/16	Mon 6/27/16	Yes		
1369	1.5.28	0%		Maintenance, Support, and Enhancement	0 hrs			No		
1379	1.6	0%		Aircraft	18,338 hrs			No		
1380	1.6.1	0%		Aircraft High Level Estimated Hours	18,338 hrs			No		
1381	1.6.2	0%		Phase Initiation	0 hrs	Wed 4/2/14	Wed 4/2/14	Yes		
1382	1.6.3	0%		Aircraft Registration	0 hrs			No		
1383	1.6.4	0%		Cross Functional Integration	0 hrs			No		
1392	1.6.5	0%		User Acceptance Testing	0 hrs	Fri 3/6/15	Fri 3/6/15	Yes		
1393	1.6.6	0%		Employee Readiness	0 hrs	Fri 3/6/15	Fri 3/6/15	Yes		
1398	1.6.7	0%		Deployment	0 hrs			No		
1410	1.6.8	0%		Activation	0 hrs	Fri 7/10/15	Fri 7/10/15	Yes		
1411	1.6.9	0%		Stabilization	0 hrs			No		
1412	1.6.10	0%		Transition	0 hrs	Mon 1/4/16	Mon 1/4/16	Yes		
1413	1.6.11	0%		Maintenance, Support, and Enhancement	0 hrs			No		
1423	1.7	0%		Title and Registration	95,850 hrs			No		

ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter	
									Mar	Oct
1424	1.7.1	0%		Title and Registration High Level Estimate Hours	95,850 hrs			No		
1425	1.7.2	0%		Phase Initiation	0 hrs	Wed 4/2/14	Wed 4/2/14	Yes		
1426	1.7.3	0%		AAMVA - NMVTIS	0 hrs			No		
1433	1.7.4	0%		Lien Application	0 hrs			No		
1439	1.7.5	0%		Abandoned Vehicle	0 hrs			No		
1441	1.7.6	0%		Vehicle Management	0 hrs			No		
1453	1.7.7	0%		Electronic Lean and Title	0 hrs			No		
1456	1.7.8	0%		Real Time Inquiries	0 hrs			No		
1472	1.7.9	0%		Mandatory Insurance	0 hrs			No		
1476	1.7.10	0%		Title	0 hrs			No		
1490	1.7.11	0%		Mobile Home	0 hrs			No		
1492	1.7.12	0%		Plates	0 hrs			No		
1502	1.7.13	0%		Registration	0 hrs			No		
1514	1.7.14	0%		Vehicle Permits	0 hrs			No		
1518	1.7.15	0%		Plate Credit	0 hrs			No		
1521	1.7.16	0%		Trusted Party	0 hrs			No		
1522	1.7.17	0%		IRP Integration	0 hrs			No		
1524	1.7.18	0%		IFTA Integration	0 hrs			No		
1525	1.7.19	0%		CVIEW - CVISN Integration	0 hrs			No		
1526	1.7.20	0%		Confidential and Fictitious	0 hrs			No		
1529	1.7.21	0%		Cross Functional Integration	0 hrs			No		
1536	1.7.22	0%		User Acceptance Testing	0 hrs	Fri 7/7/17	Fri 7/7/17	Yes		
1537	1.7.23	0%		Employee Readiness	0 hrs	Fri 7/7/17	Fri 7/7/17	Yes		
1542	1.7.24	0%		Deployment	0 hrs			No		
1554	1.7.25	0%		Activation	0 hrs	Mon 1/8/18	Mon 1/8/18	Yes		
1555	1.7.26	0%		Stabilization	0 hrs			No		
1556	1.7.27	0%		Transition	0 hrs	Mon 1/7/19	Mon 1/7/19	Yes		
1557	1.7.28	0%		Maintenance, Support, and Enhancement	0 hrs			No		
1567	1.8	0%		Drivers	95,850 hrs			No		
1568	1.8.1	0%		Drivers High Level Estimated Hours	95,850 hrs			No		


ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter	
									Mar	Oct
1569	1.8.2	0%		Phase Initiation	0 hrs	Wed 4/2/14	Wed 4/2/14	Yes		
1570	1.8.3	0%		AAMVA	0 hrs			No		
1575	1.8.4	0%		Driver Record / Control	0 hrs			No		
1582	1.8.5	0%		CDL	0 hrs			No		
1585	1.8.6	0%		Confidential and Fictitious	0 hrs			No		
1588	1.8.7	0%		Driver License Issuance	0 hrs			No		
1593	1.8.8	0%		Cross Functional Integration	0 hrs			No		
1602	1.8.9	0%		User Acceptance Testing	0 hrs	Fri 7/6/18	Fri 7/6/18	Yes		
1603	1.8.10	0%		Employee Readiness	0 hrs	Fri 7/6/18	Fri 7/6/18	Yes		
1608	1.8.11	0%		Deployment	0 hrs			No		
1620	1.8.12	0%		Activation	0 hrs	Mon 1/7/19	Mon 1/7/19	Yes		
1621	1.8.13	0%		Stabilization	0 hrs			No		
1622	1.8.14	0%		Transition	0 hrs	Mon 1/6/20	Mon 1/6/20	Yes		
1623	1.8.15	0%		Maintenance, Support, and Enhancement	0 hrs			No		
1634	1.9	0%		Licensing and Contracting	22,388 hrs			No		
1635	1.9.1	0%		Licensing and Contracting High Level Estimated Hours	22,388 hrs			No		
1636	1.9.2	0%		Phase Initiation	0 hrs	Wed 4/2/14	Wed 4/2/14	Yes		
1637	1.9.3	0%		Permits	0 hrs			No		
1638	1.9.4	0%		Issue New License	0 hrs			No		
1639	1.9.5	0%		Update License	0 hrs			No		
1640	1.9.6	0%		Cancel License	0 hrs			No		
1641	1.9.7	0%		Reprint Tabs	0 hrs			No		
1642	1.9.8	0%		Renew License	0 hrs			No		
1643	1.9.9	0%		Reprint License	0 hrs			No		
1644	1.9.10	0%		Plates	0 hrs			No		
1649	1.9.11	0%		Reports	0 hrs			No		
1661	1.9.12	0%		Licensing Archive Dealer Licenses	0 hrs			No		
1662	1.9.13	0%		Licensing Correspondence	0 hrs			No		
1663	1.9.14	0%		Licensing Excess Lost/Stolen Plates	0 hrs			No		
1664	1.9.15	0%		Licensing Expired Manufacturers	0 hrs			No		


ID	WBS	% Complete	Task Mode	Task Name	Work	Start	Finish	Milestone	Quarter	
									Mar	Oct
1665	1.9.16	0%		Licensing Privilege Revocation	0 hrs			No		
1666	1.9.17	0%		Licensing Purge On Hold Licenses	0 hrs			No		
1667	1.9.18	0%		Cross Functional Integration	0 hrs			No		
1672	1.9.19	0%		Licensing Integration	0 hrs			No		
1673	1.9.20	0%		Finance Integration	0 hrs			No		
1674	1.9.21	0%		Title and Registration Integration	0 hrs			No		
1675	1.9.22	0%		User Acceptance Testing	0 hrs	Fri 1/4/19	Fri 1/4/19	Yes		
1676	1.9.23	0%		Employee Readiness	0 hrs	Fri 1/4/19	Fri 1/4/19	Yes		
1681	1.9.24	0%		Deployment	0 hrs			No		
1693	1.9.25	0%		Activation	0 hrs	Mon 7/8/19	Mon 7/8/19	Yes		
1694	1.9.26	0%		Stabilization	0 hrs			No		
1695	1.9.27	0%		Transition	0 hrs	Mon 1/6/20	Mon 1/6/20	Yes		
1696	1.9.28	0%		Maintenance, Support, and Enhancement	0 hrs			No		
1706	1.10	0%		Project Close	0 hrs			No		


1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		
Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun	Jan	Aug	Mar	Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun

1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		
Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun	Jan	Aug	Mar	Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun



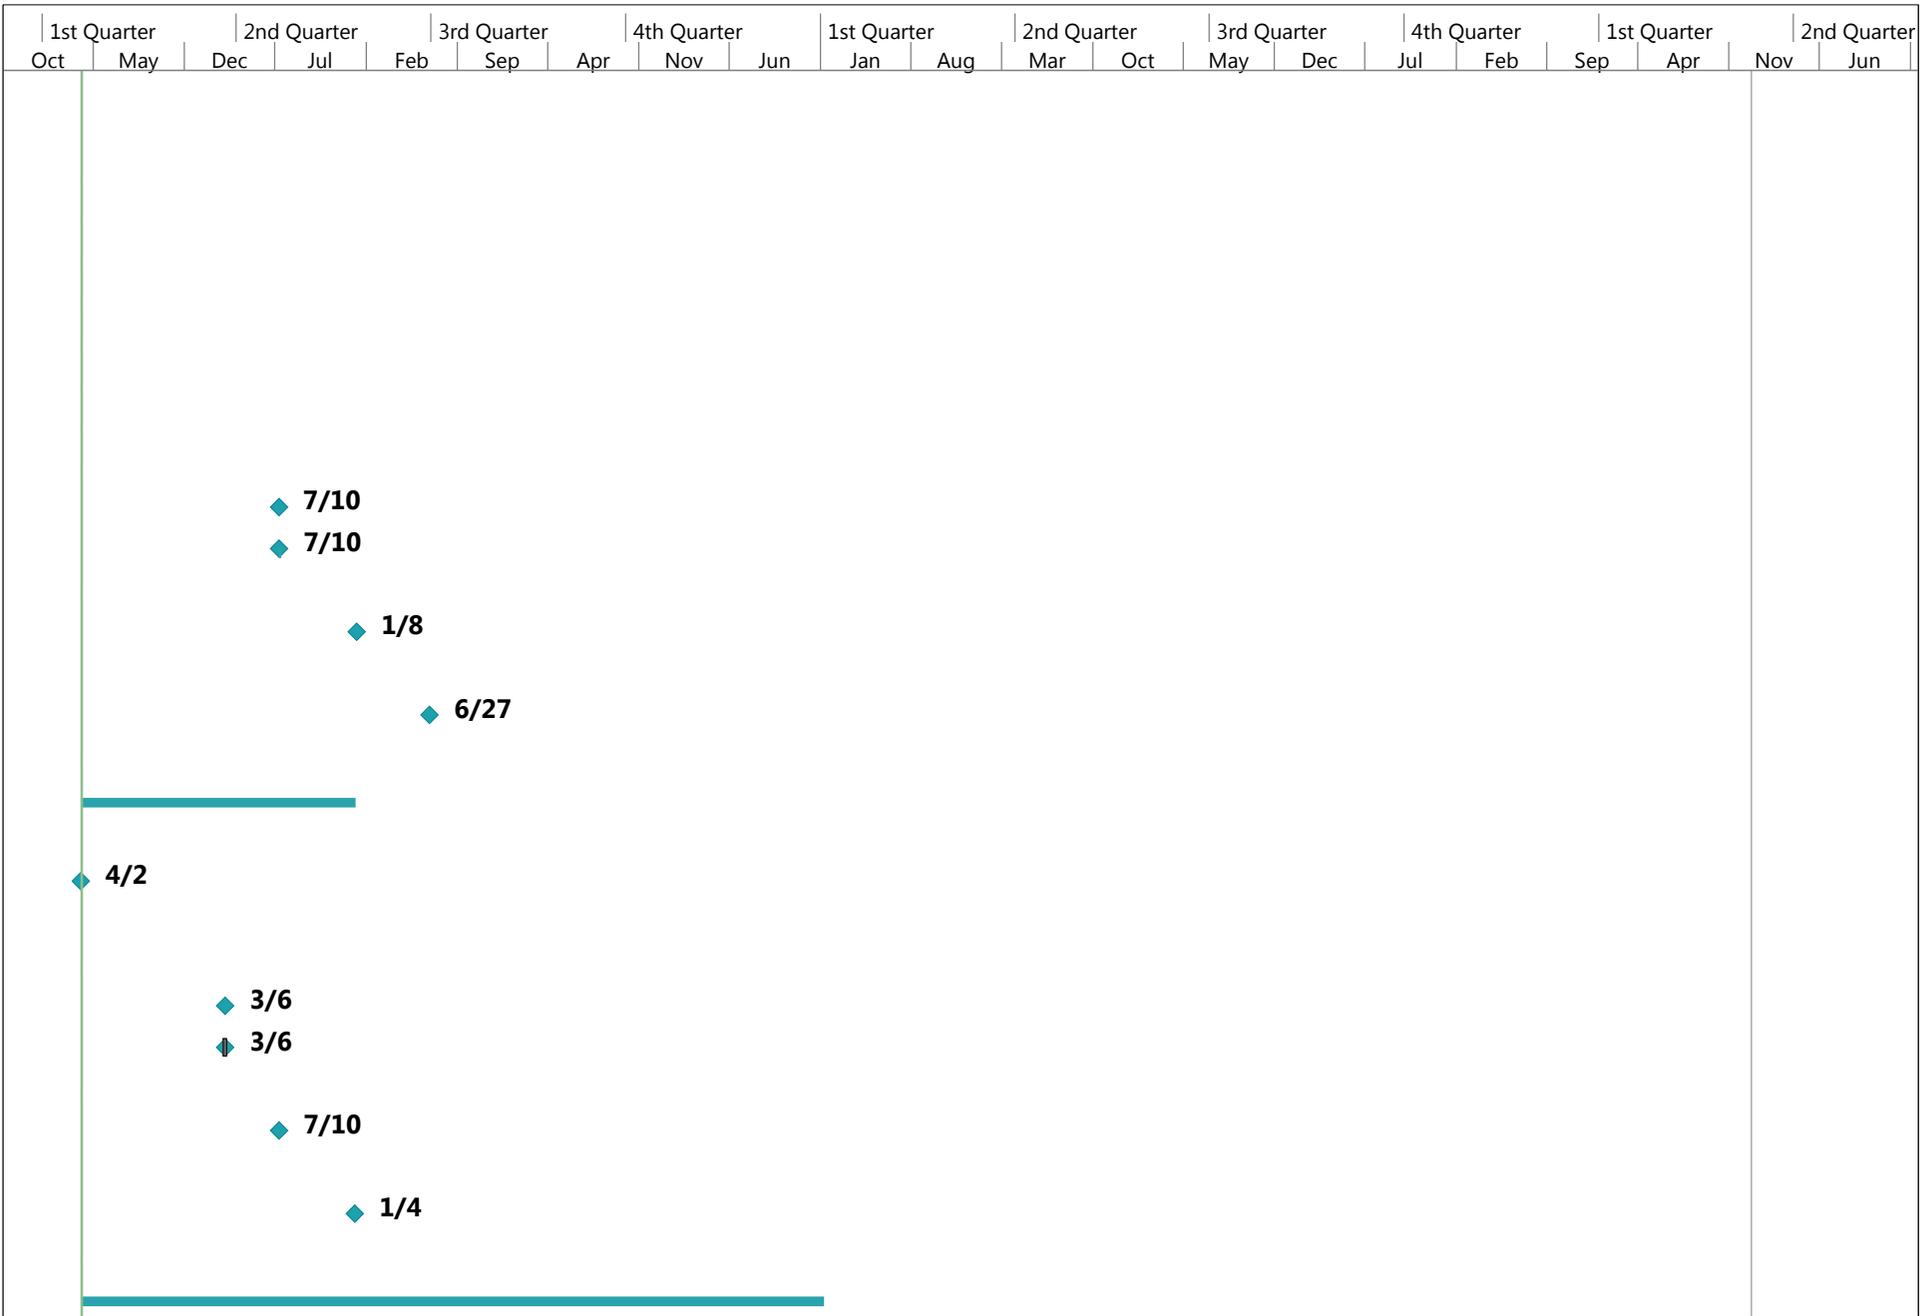

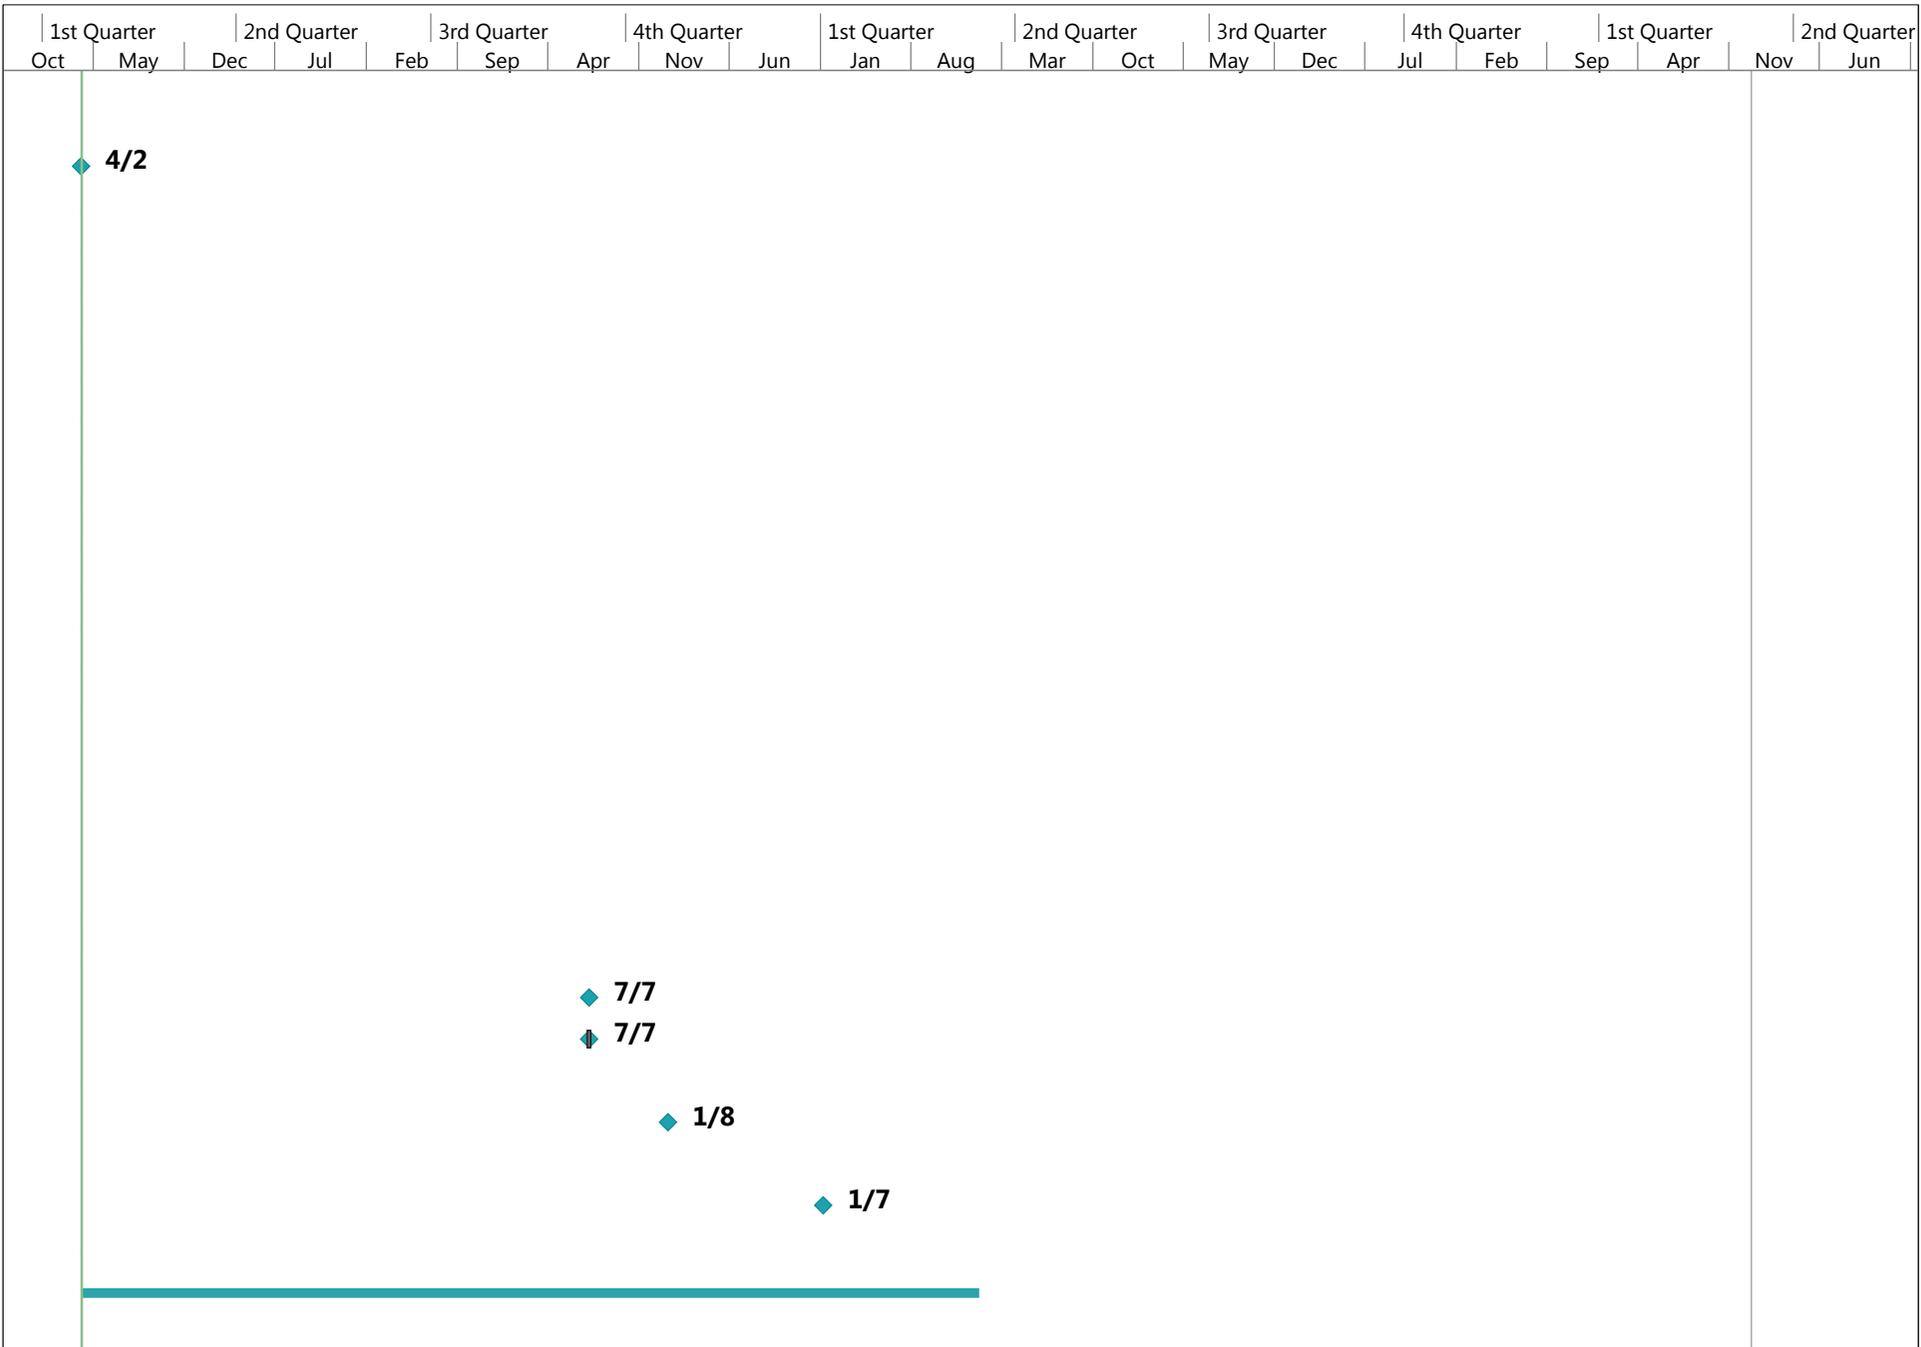

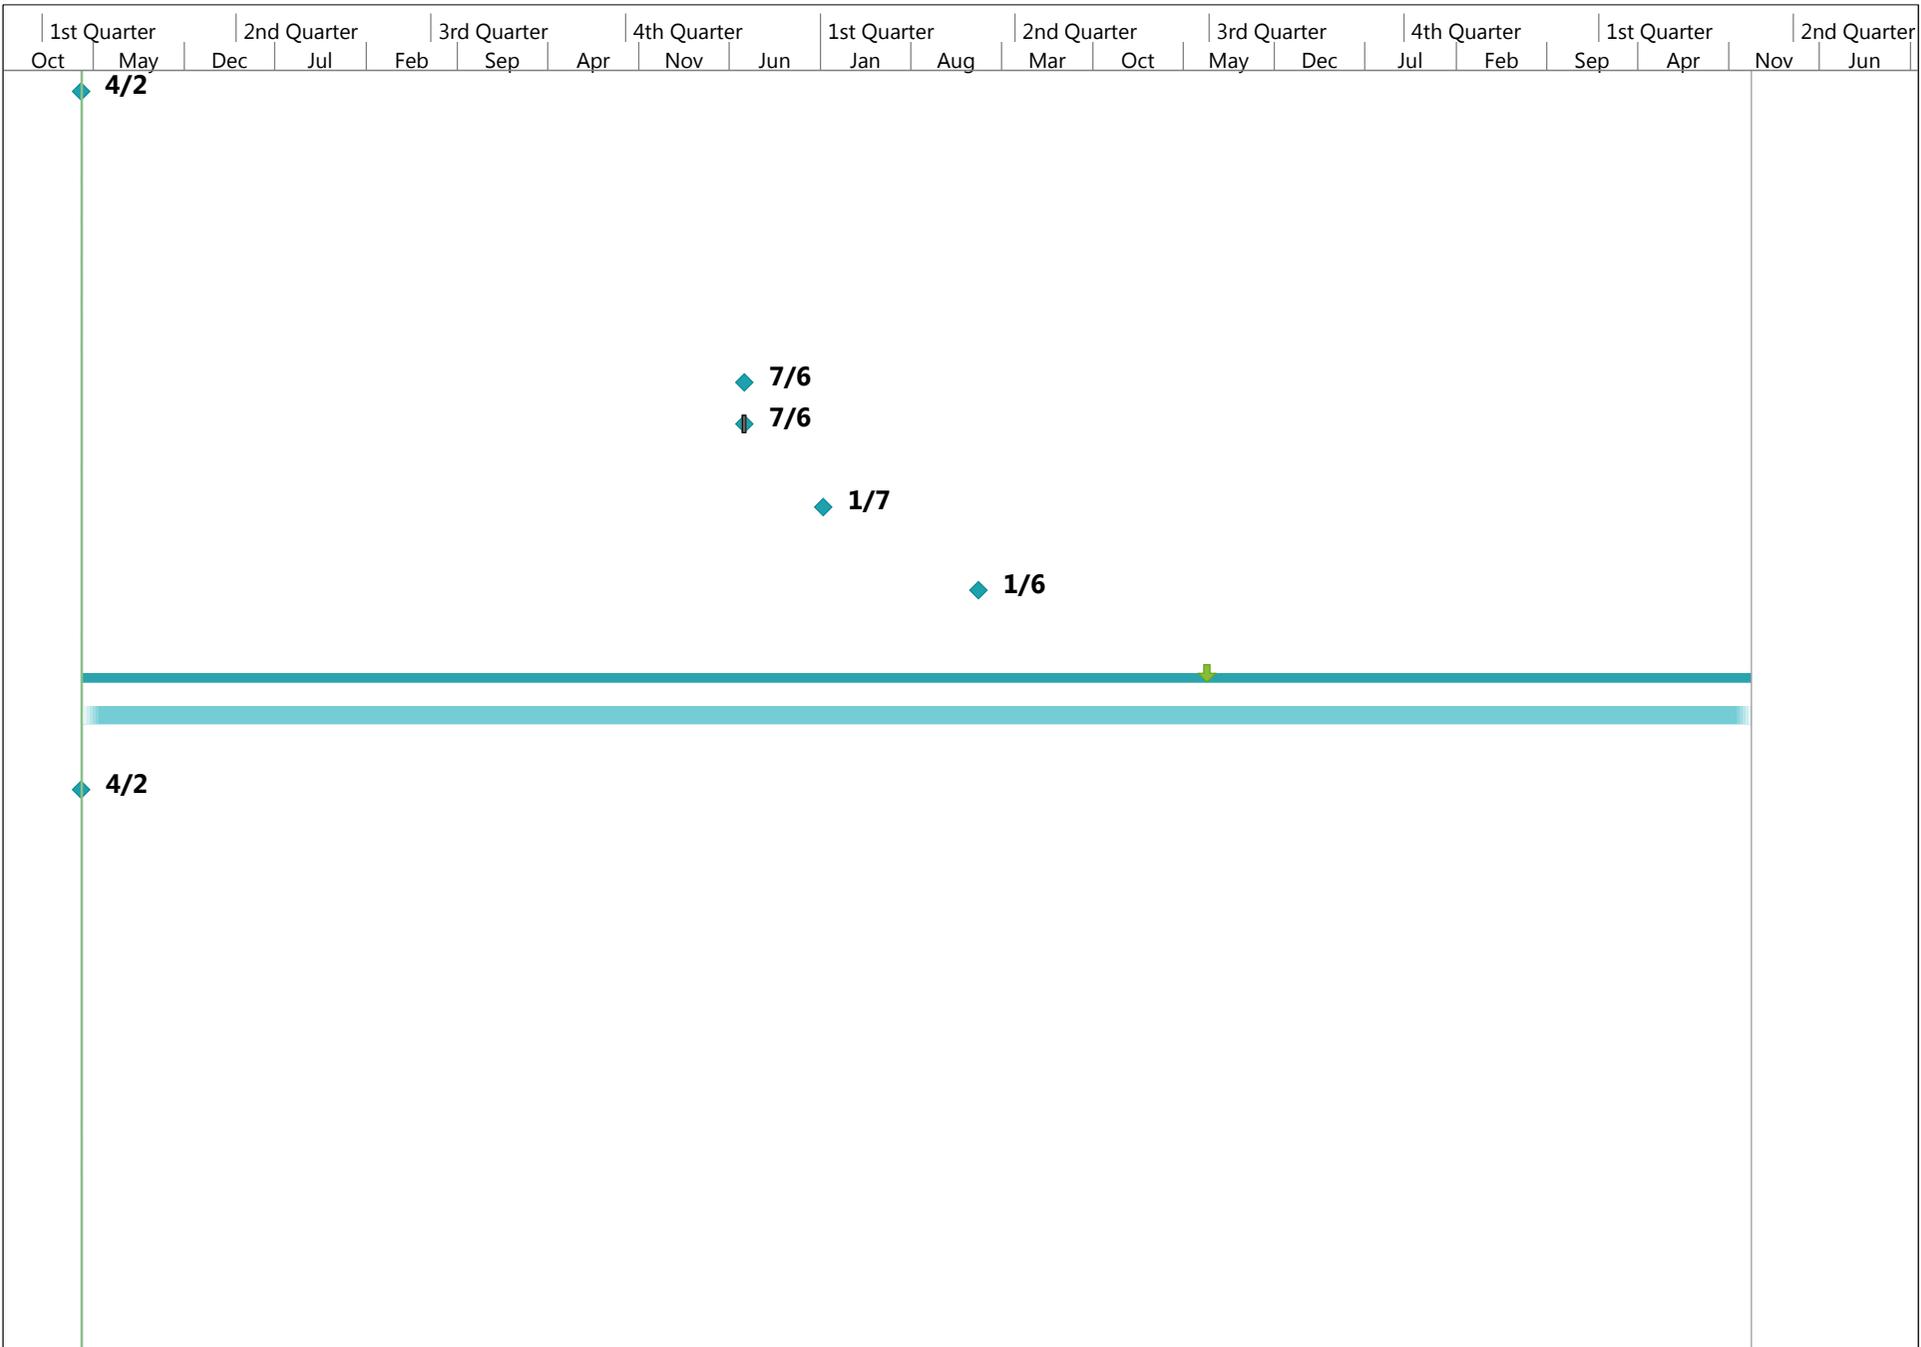

1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		
Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun	Jan	Aug	Mar	Oct	May	Dec	Jul	Feb	Sep	Apr	Nov	Jun
<p>◆ 1/4</p> <p>◆ 1/4</p> <p>◆ 7/8</p> <p>◆ 1/6</p>																				
